

Team Roles & Workstreams

June 2025 | *Action Items · M1 To-Do · Process Flow · Welcome Email · Roles & Responsibilities · Workstreams · Dependencies · Phase Cards · Cadence · GitHub Guide*

COLOUR KEY:

 Munish

 Shefali

 Hansh

 Eddie

 Yash

 TBD

Each colour identifies one person consistently across all slides in this deck.

Action Items — June 9 Group Meeting

Tasks agreed at the first full team meeting. Status reflects current state as of June 10.

OWNER	ACTION ITEM	WHEN	STATUS
Eddie	Confirm Om Maheshwari: interest and availability for editing and/or music role. Report back to Munish.	M1 Wk1	Pending
Munish	Add Yash's suggestion: highlight individual contributions and value received from cohort members in the documentary questionnaire.	M1	Pending
Munish	Reach out to Sagar Batra (content/event marketing) and Om Maheshwari (music) as roles are confirmed and when ready.	M1	Pending
Shefali	Mentor/transfer Project Manager (PM) responsibilities to a detail-oriented team member. Shefali is temp PM.	M2	Pending
Shefali	Simplify the playbook into a deck so it is easily digestible for the whole team.	M1	✓ Done
Munish + Shefali	Update Roles & Responsibilities from June 9 meeting decisions.	M1	✓ Done
Yash	Take ownership of marketing/distribution role. Coordinate with Munish on content. Begin planning social media and promotional activities.	M1	Pending
All	Review the playbook. Clarify and accept roles. Inform Munish of any role changes or additional support needs.	M1 Wk1	Pending
All	Be diligent in organising and naming all documentary footage as it is collected. Follow folder structure and best practices in the playbook.	Ongoing	Pending
All	Legal and branding: do not reference '100X' publicly. Use 'learning community'. Shefali's guidance.	Ongoing	Pending

Action Items — June 9 Post-Meeting

Decisions from the Shefali + Munish session after the group meeting.

OWNER	ACTION ITEM	WHEN	STATUS
Shefali	Send questionnaire to all 30 ACES members. Participants self-select: tick a box if they want to be a protagonist. Shortlist 5 from responses.	M1 Wk1	Pending
Shefali	Create and distribute protagonist selection rubric (scores on specificity, emotional stakes, contrast potential, surprise factor).	M1 Wk1	✓ Done
Shefali	Retain Project Manager (PM) role for now. Identify and begin mentoring a detail-oriented second person for PM. Not urgent until M2.	M2	Pending
Shefali	Begin outreach to find an Indian entertainment lawyer or advisor. Not needed until M3+. Do not use '100X' publicly — use 'learning community'.	M3+	Pending
Eddie	Confirm with Om Maheshwari: interest in editing and/or music role. Om sits as sub-role under Eddie's or Hansh's workstream.	M1 Wk1	Pending
Munish	Reach out to Sagar Batra for content/event marketing sub-role under Yash's workstream when ready.	M1	Pending
Munish	Decide budget ownership: Hansh, Shefali, or future Producer? This is blocking the budget line in the playbook.	M1	Pending
Munish	Clarify Exec/Producer definition with Shefali before Netflix pitch. Not blocking immediate production.	M2	Pending
Hansh	Set up GitHub repository and full folder structure before M2 filming begins. Nothing gets filmed until this system exists.	M1 Wk1	Pending
All	Weekly async update to GitHub README by each workstream owner every Friday. WhatsApp for urgent decisions only. Bilateral Zoom if thread exceeds 5 messages.	Ongoing	Pending

Roles & Responsibilities

Colour = person. Consistent across all slides in this deck.

TITLE(S)	NAME	WHAT THEY OWN	WHERE TEAM CROSS-SUPPORTS THEM
Director	Munish Bhardwaj	Creative vision, story direction, picture lock, Netflix relationship, music sign-off, weekly meeting chair, tiebreaker on all decisions.	Shefali manages scheduling. Director reviews footage.
Showrunner / Narrator / Story Producer / PM (temp)	Shefali Mody + Eddie	Questionnaire to all 30 (M1). Zoom interviews of the 5 selected protagonists (with Eddie). Weekly prompts. Character arc & story bible. All Project Manager (PM) duties. Cut review coordination.	Munish owns all editorial. Eddie/Munish & Shefali review initial content.
Director of Photography	Eddie Bhardwaj	Hardware tech — call to understand each protagonist's working environment. Camera angles to record. Settings for same footage from different angles.	Shefali briefs on story priorities. Hansh provides ingest system.
Post Production (+ Om Maheshwari)	Hansh Goyal	Editing, file video, WhatsApp archive, archival footage, storage & categorisation, sound effects & motion capture, budget tracking, colour grade, sound mix, Netflix delivery.	Shefali & Eddie view and categorise content.
Marketing & Content Strategist, Music Brief Owner (+ Sagar Batra)	Yash Javeri	Hardware audit of all 30. Screen recording & Zoom setup guide. Social media presence. Content calendar. Weekly publishing M3–M6. Music brief co-owner. Release & distribution strategy co-owner.	Hansh provides ingest system. Munish approves all public-facing content.
Exec/Producer	TBD	Budget. Face of documentary pitches. (Needs more clarity around this role definition.)	—
Music / Audio Design	TBD	Final say on sound of documentary. B-tracks. Scale. Sound effects. Ambient music. Must resolve before M5 (Aug–Sep).	—
Budget	TBD	Legal advisor coordination. Financial tracking.	—
Legal	TBD	Indian entertainment lawyer or advisor. Not needed until M3 (August).	—

Team Cadence Recommendation

Replacing Chapter 24. The team wants async — here's how to make it work.

Fully Async

GitHub + WhatsApp only

Pros

- Fits distributed volunteer team
- No scheduling stress
- Lower overwhelm

Cons

- Decisions go cold fast
- Munish's creative direction at risk
- People Operations PM load increases

Weekly Sync

Current Playbook (Ch. 24)

Pros

- Decisions made fast
- Creative direction protected
- Single alignment point

Cons

- Hard to schedule across time zones
- Volunteer team resists it
- Team called it overwhelming

✓ Recommended

Async-first + Bi-weekly Check-in

Pros

- No weekly sync
- Bi-weekly 30-min check-in / stand-up (Munish chairs)
- Weekly async README update by each workstream owner
- WhatsApp for urgent decisions only
- Bilateral Zoom if thread exceeds 5 messages

Cons

- Requires discipline on README updates
- Bi-weekly check-in is a hard commitment — no skipping

Sub-Team Member Selection Rubric

Skills, not just enthusiasm. Use when any workstream lead recruits — Om Maheshwari, Sagar Batra, or anyone else.

1. Relevant Skill

Does this person have a demonstrable skill the workstream actually needs? Not 'I've always wanted to try editing' — evidence of actual capability. Ask for examples or work samples.

0–5

2. Availability

Can they genuinely commit to async deliverables each week? Volunteer enthusiasm fades. Probe actual weekly hours available, not aspirational ones.

0–5

3. Async Discipline

Do they respond to messages? Do they follow through without being chased? One data point: have they delivered on anything in the cohort so far?

0–5

4. Alignment with Tone

Do they understand this is a real documentary, not a side project? Do they respect the participants' stories? Check for seriousness of intent.

0–5

5. Workstream Fit


Does their skill fill a specific gap in the workstream? Score higher if they complement (not duplicate) what the lead already does.

0–5

Shortlist anyone scoring 18+ · Pass at 12 or below · Discuss 13–17 with Munish before deciding

M1 Process Flow — June 2025

The sequence within Month 1. Each step is a dependency for the next. Colour = person responsible.

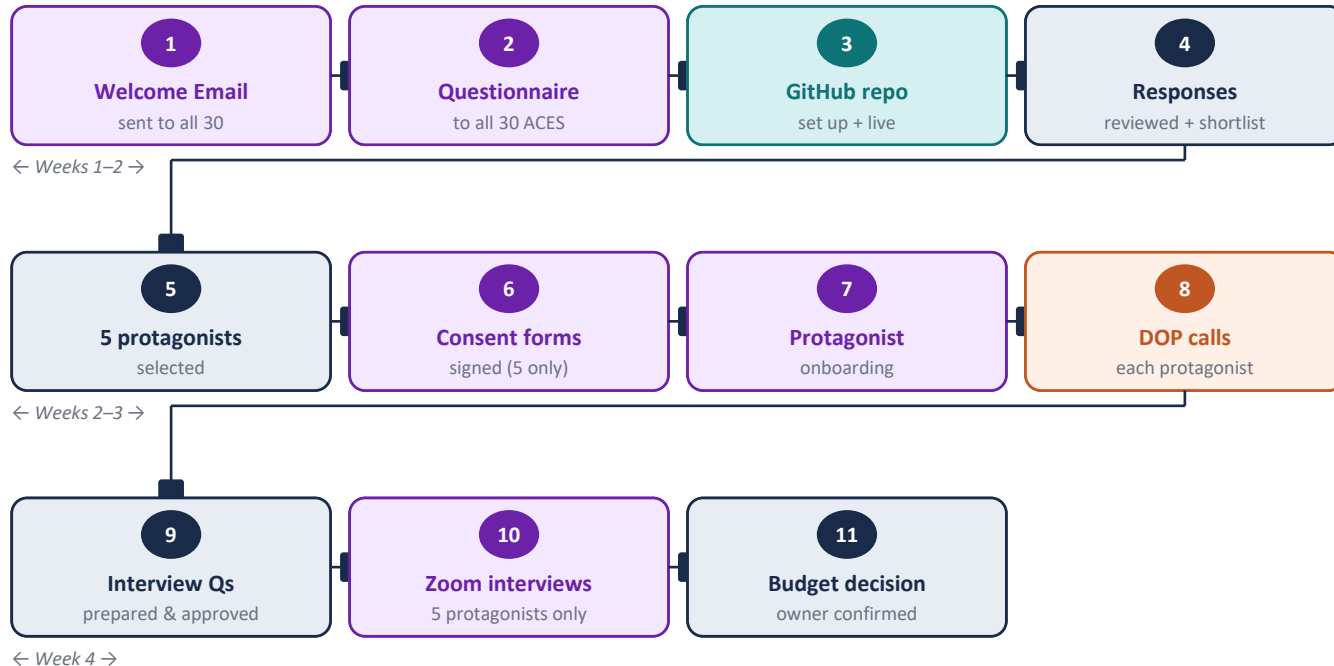

M1 To-Do List — June 2025

Not a new list — the action items from both meetings, sequenced by dependency. Each item must be done before the next begins.

OWNER	ACTION ITEM	WHEN	STATUS
Shefali	Finalise and send Welcome Email to all 30 ACES members. Include the link to the questionnaire. (Email template on next slide.)	Wk 1	Pending
Shefali	Send questionnaire to all 30. Participants self-select protagonist interest by ticking a box. Collect all responses.	Wk 1	Pending
Hansh	Set up GitHub repository. Create folder structure. Add README with workstream sections and Friday update format. Share access with all 5 team members.	Wk 1	Pending
Munish + Shefali	Review all questionnaire responses together. Apply the selection rubric. Identify 5 protagonists.	Wk 2	Pending
Shefali	Send consent forms to the 5 selected protagonists. Simple sign-off only — no legal review needed at this stage.	Wk 2	Pending
Shefali	Schedule and run protagonist onboarding session (group). Cover: what it means to be a protagonist, filming setup, hardware, what comes next.	Wk 3	Pending
Eddie	Begin DOP calls with each of the 5 protagonists. Understand their working environment. Camera angles, settings, lighting. Confirm hardware setup.	Wk 3	Pending
Munish + Shefali	Draft protagonist story arc notes (informal). What do we expect from each person's arc? This informs the Zoom interview questions.	Wk 3	Pending
Shefali + Eddie	Zoom interviews — the 5 selected protagonists only. Shefali leads. Eddie as second. These become the film's backbone.	Wk 4	Pending
Munish	Decide budget ownership: Hansh, Shefali, or future Producer? Make the call — this is blocking the budget line in the playbook.	Wk 4	Pending

The 5 Workstreams

Read your workstream. Colour = your person. Names match exactly across this deck and the Roles & Responsibilities slide.



Story & Creative

Munish + Shefali

- Narrative arc & story bible
- Questionnaire (all 30 ACES)
- Protagonist selection rubric
- Weekly prompts (Shefali)
- Cut direction & picture lock



People Operations

Shefali + Eddie (PM temp)

- Scheduling & participant comms
- Consent forms (5 protagonists)
- Protagonist onboarding
- Zoom interviews — 5 only (Shefali + Eddie)
- GitHub README updates



Content & Post

Hansh (+ Om Maheshwari)

- File system & naming
- WhatsApp archive
- Archival footage (ACES)
- Colour grade & sound mix
- Netflix delivery



Hardware & Tech

Eddie (+ Om TBD)

- DOP setup — call each protagonist
- Camera angles & settings
- Same footage from different angles
- Screen recording guide
- Graduation day camera



Marketing & Distribution

Yash (+ Sagar Batra TBD)

- Social media & content calendar
- Weekly publishing from M3
- Release & distribution strategy
- Festival submissions
- Hardware audit of all 30

Phase Cards — What Happens When

Compressed to real timeline. Celebration event target: mid-September.

M1	M2	M3–M4	M5	M6 + Event
June Development • Concept & Netflix pitch (Munish + Shefali) • Questionnaire to all 30 ACES (Shefali) • Consent forms, budget, music brief (Hansh + Munish) • GitHub repo + folder structure (Hansh) • Protagonist selection + onboarding • DOP calls begin (Eddie)	July Pre-Production • DOP setup complete — all protagonists (Eddie) • Questionnaire responses reviewed — shortlist 5 • Zoom interviews — 5 protagonists only (Shefali + Eddie) • Protagonist story arc briefs (Munish + Shefali) • Content & social strategy live (Yash)	August Production • Weekly prompts every Monday (Shefali) • Self-shot footage arriving (Hansh manages files) • WhatsApp archive daily (Hansh) • Weekly content publishing (Yash — Munish approves) • Story bible updated every Friday (Shefali)	Aug–Sep Post-Production • Paper edit → rough cut → fine cut (Om + Hansh) • Narrator script + recording if needed (Shefali) • Cut review feedback forms (Eddie + Munish) • Colour grade, sound mix (Hansh) • Music clearance (Munish)	September Delivery + Celebration • QC + legal clearances (Shefali + Hansh) • Netflix submission (Munish + Hansh) • Marketing assets + release activation (Yash) • 🎉 Celebration event — mid-September • Munish + Shefali sign off

Workstream Dependencies

Real months shown. Compressed to fit September celebration event. Outlined bars = active. Colour = lead person.

WORKSTREAM	June M1	July M2	August M3–M4	Aug–Sep M5 Post	Sep Delivery	Mid-Sep Event
● Story & Creative	Concept + pitch	Protagonist selection	Story bible + prompts	Paper edit + narration	Sign off	
● People Operations	Consent + onboard	Interviews + comms	Prompts + comms	Cut review	Legal clearance	
● Content & Post	File system setup		Archive + footage in	Edit + grade + sound	Netflix delivery	
● Hardware & Tech		DOP calls + setup	Recording support			Event camera
● Marketing & Distrib.	Strategy + setup	Content strategy	Weekly publishing	Build audience	Release launch	Event promo

Key Dependencies:

- File system (June M1) must exist before ANY footage is uploaded
- DOP calls (July M2) must complete before protagonist recording begins
- Protagonist selection (June) unlocks People Operations onboarding
- Content & Post edit (Aug–Sep M5) depends on Story & Creative paper edit completing first
- Music/Audio Design must be confirmed owner before M5 (Aug–Sep) begins

Welcome Email — For Approval

Sent by Shefali to all 30 ACES members, Week 1 of June. Peer-to-peer tone — not a formal production announcement.

FROM: Shefali Mody | TO: All 30 ACES members (BCC) | SUBJECT: Something we're building — and I need your help (5 min read)

Hi [Name],

I want to tell you about something that's happening alongside this program — and to ask if you'd like to be part of it.

I'm one of you. I'm in this cohort, doing this course, trying to build something with AI that I've never built before. And somewhere in the chaos of the first week I started thinking: this story is extraordinary. And somebody should capture it.

So we're making a documentary. Not a polished, corporate, 'here's-what-AI-can-do' documentary. A real one. About what it actually feels like to be a non-technical person thrown into a room with 29 strangers from around the world, all trying to learn something hard together, all secretly terrified, all somehow becoming each other's support system.

Munish Bhardwaj is directing it. He's also making a documentary for the first time — which, as you might appreciate, fits the theme perfectly.

Here's what I'm asking: a short questionnaire. Nothing technical. Just honest answers about where you are and what this means to you. At the end, you can say whether you'd like to be in the documentary — and whether you'd like to be considered as one of five protagonists we follow in depth. Both completely optional.

Takes about 15 minutes. No right answers. [\[LINK TO QUESTIONNAIRE\]](#)

ACTION REQUIRED: Munish to review and approve this email before Shefali sends. Reply with any changes.

All-30 Questionnaire — For Approval

Sent to all 30 ACES members with the Welcome Email. Self-completion. Includes opt-in checkbox for protagonist interest.

ACTION REQUIRED: Munish to review and approve before Shefali sends. Estimated 15 minutes for participants to complete.

PART A — Starting Point

1. What is your background? (profession, industry, country)
2. Have you ever built an app or written code before?
3. On a scale of 1–10, how technical do you consider yourself?
4. What made you join the 100X program?

PART B — Your Why

1. What app are you trying to build, and why does it matter to you?
2. What is the thing you are most afraid of in this process?
3. What would it mean to you if this actually worked?
4. What does 'success' look like for you personally at the end of this?

PART C — Your Story

1. Is there a moment — in life or work — that led you here? Describe it.
2. What have you tried to build or create before that didn't work? What happened?
3. What do the people closest to you think about what you're doing?

PART D — Hardware & Filming Logistics

1. What device do you work on most? (laptop/desktop/tablet — model if you know it)
2. Do you have a decent webcam or external camera available?
3. Are you comfortable recording short clips of yourself working? (screen + face)
4. What is your available filming environment? (home office, café, shared space, other)

PART E — Documentary Opt-In

1. ☐ I am happy for my responses to be used as background context for the documentary.
2. ☐ I would like to be considered as one of five protagonists followed in depth. (This means regular filming, Zoom interviews, and sharing your journey in real time.)
3. ☐ I do NOT wish to participate beyond this questionnaire. (No further contact.)

Protagonist Selection Rubric

Used after questionnaire responses are in. Shefali and Munish score each respondent independently, then compare. Target shortlist: 8–10 candidates.

✓ **DONE** — Rubric created and distributed. Apply when questionnaire responses are in (M1 Week 2).

1 Specificity

Are their answers specific and personal — or generic and polished? Specific fear beats vague fear. A named person in the stakes question scores higher than 'my family'. Look for: proper nouns, exact moments, concrete consequences.

0–1 Generic answers. Could apply to anyone. 4–5 Answers that only this person could give.

2 Emotional Stakes

Is there something genuinely at risk for this person? Not just 'I want to learn' — something where failure would actually hurt. Look for: career pivots, personal proving grounds, people they need to show something to, things they've already failed at.

0–1 Learning goal. Safe aspiration.

4–5 Real cost to failing. Real person watching.

3 Contrast Potential

Does this person offer something different from the others already on the shortlist? The ensemble needs contrast — age, country, background, starting point, archetype. Score higher if they fill a gap. Score lower if they duplicate someone already shortlisted.

0–1 Similar to someone already on the list.

4–5 Fills a gap — age, country, archetype, starting point.

4 Surprise Factor

Did any answer genuinely surprise you? Did they subvert an assumption? Did they say something you didn't expect from someone in their situation? The wildcard protagonist lives here. Even one surprising answer is worth noting.

0–1 Answers landed as expected.

4–5 At least one answer stopped you. You didn't see it coming.

SCORING: Each criterion is scored 0–5. Maximum score: 20 · Shortlist target: score 14+ · Discuss 10–13 with Munish · Pass below 10

Protagonist Zoom Interview Questions — For Approval

Used in Step 10: Zoom interviews with the 5 selected protagonists only. Shefali leads. Eddie as second. ~60 minutes per person.

ACTION REQUIRED: Munish to review and approve before interviews begin. These become the film's primary source material.

Opening — Identity & Starting Point	Doubt & Pressure
● Before we start — how are you feeling right now, on the eve of building something you've never built before?	● What's the thing you're most afraid of in this process? Not the practical fear — the deeper one.
● Tell me who you are. Not your job title — who you actually are, and how you ended up here.	● Is there a moment you can think of when you almost stopped? What kept you going?
● What did the people in your life say when you told them what you were doing?	● Who is this for? Is there a specific person — real or imagined — whose life this would change?
The Decision	Stakes & Closing
● What's the idea you're building, and where did it come from? Was there a specific moment?	● What would it mean — really mean — to you if this worked? And what would it mean if it didn't?
● What have you tried to build or create in the past that didn't work? What happened, and what did you do with that?	● Six months from now, what do you hope you can say about this experience?
● What do you believe that most people around you don't? About technology, about yourself, about what's possible?	● Is there anything nobody has asked you yet — about this, about you — that you wish they would?

GitHub — How We Use It

GitHub is where all production documents live. The README is the team's shared pulse. Updated every Friday by each workstream owner.

5 Things You Need to Be Able to Do

- 1 Open the repo in a browser
Go to github.com → find the Zero to Hero repo → bookmark it.
- 2 Read the README
The README is on the front page of the repo. This is your weekly status update.
- 3 Edit your section of the README
Click the pencil icon. Find your workstream section. Update your 3 lines. Click 'Commit changes'.
- 4 Upload a file
Drag and drop your file into the right folder. Add a commit message. Click 'Commit changes'.
- 5 You will NOT break anything
GitHub keeps a full history. Every change can be undone. There is no deleting by accident.

Your Friday README Update — 3 Lines

STATUS:	On track / At risk / Blocked
THIS WEEK:	One sentence on what happened
NEXT WEEK:	One sentence on what's coming

Repo Folder Structure

- FROM-ZERO-TO-APP/ (root)
 - 01-PARTICIPANTS/ → one folder per person
 - 02-WHATSAPP-ARCHIVE/ → screenshots (Hansh)
 - 03-STORY-BIBLE/ → all versions (Shefali)
 - 04-SELECTS/ → Eddie's selects by week
 - 05-EDIT/ → all cut versions
 - 06-DELIVERY/ → final Netflix package
 - 07-PRODUCTION-DOCS/ → RACI, Gantt, budget
 - README.md → team status (updated Fridays)

FILE NAMING RULE: [FIRSTNAME-LASTNAME]_[W##]_[TYPE]_[YYYY-MM-DD].[ext] e.g. SHEFALI-MODY_W03_SELF-SHOT_2025-03-17.mp4 —
No spaces. Ever.
